Gateway Blvd/Calgary Tr. 23 Avenue Interchange
2009 Construction Schedule
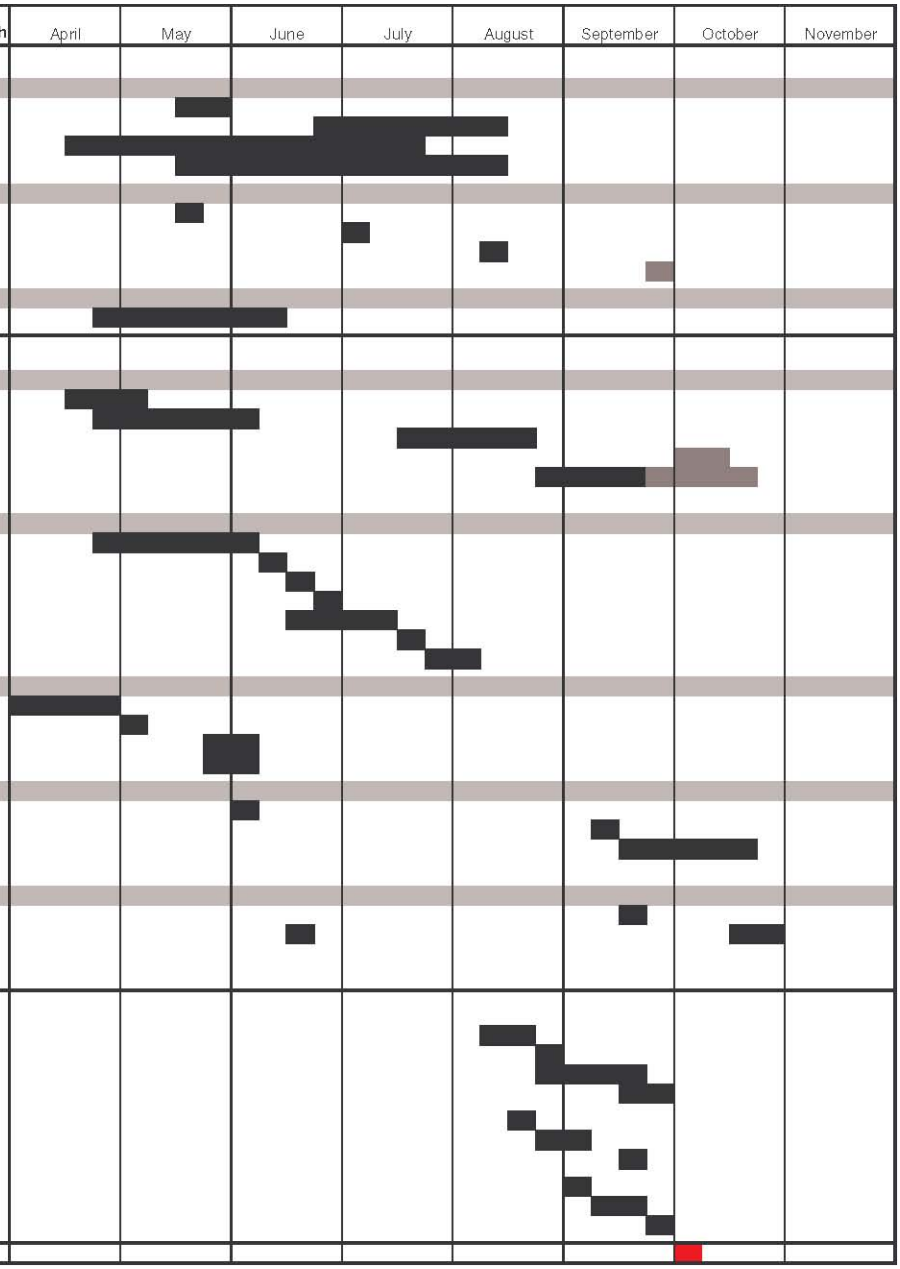
Activity	Scheduled Start	Scheduled Finish
Roadworks		
NWSR		
Complete paving full width to "turnaround"	13-May	29-May
Complete "turnaround" to 23Ave	26-Jun	18-Aug
MSE Wall L	15-Apr	20-Jul
MSE Wall K	21-May	17-Aug
19Ave Permanent		
Stage 1 - Two way traffic on Calgary Trail	20-May	
Stage 2 - Split traffic, NB onto permanent	2-Jul	
Stage 3 - Two way traffic on Gateway Blvd.	13-Aug	
Stage 4 - Split traffic (final stage)	22-Sep	
23Ave West Widening		
Removals, CSS, GBC, C&G, Paving	20-Apr	12-Jun
Structures		
19th Avenue Overpass		
Pier shaft construction	17-Apr	8-May
South Abutment	28-Apr	3-Jun
North Abutment	15-Jul	25-Aug
Pier Cap Construction/tensioning	30-Sep	15-Oct
Girder Erection	25-Aug	23-Oct
Deck Pours	Possible Late 2009 or early 2010	
Gateway Westbound		
Deck Formwork/rebar	24-Apr	7-Jun
Stage 1 Deck Pour	8-Jun	
Stage 2 Deck Pour	15-Jun	
Stage 3 Deck Pour	26-Jun	
Concrete Barriers	17-Jun	16-Jul
Light Poles Install	16-Jul	
Approach Slabs	29-Jul	5-Aug
CPR Westbound		
Deck Formwork/rebar	30-Mar	1-May
Deck Pour	4-May	
Barriers	29-May	9-Jun
Approach Slabs	29-May	4-Jun
Gateway Eastbound		
Abutment 1 Pour	4-Jun	
Abutment 2 Pour	15-Sep	
Girders	16-Sep	23-Oct
Deck Formwork/rebar	Possible Late 2009 or early 2010	
CPR Eastbound		
Abutment 1 Pour	16-Sep	
Abutment 2 Pour	18-Jun	
Girders	13-Oct	21-Oct
Deck Formwork/rebar	Possible Late 2009 or early 2010	
Opening Westbound Structures		
Westbound ramps - CSS	11-Aug	25-Aug
Westbound ramps - GBC	26-Aug	1-Sep
Westbound ramps - C&G	27-Aug	22-Sep
Westbound ramps - Paving	18-Sep	23-Sep
Calgary Tr. SB to 23Ave Ramp - GBC	20-Aug	21-Aug
Calgary Tr. SB to 23Ave Ramp - C&G	24-Aug	8-Sep
Calgary Tr. SB to 23Ave Ramp - Paving	15-Sep	21-Sep
23Ave NB to Gateway Ramp - GBC	1-Sep	4-Sep
23Ave NB to Gateway Ramp - C&G	7-Sep	21-Sep
23Ave NB to Gateway Ramp - Paving	28-Sep	2-Oct
OPEN TRAFFIC ONTO WESTBOUND STRUCTURE	**4-Oct**
